

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors | Resource Names | 3 | Thu |
|----|-----------|--|----------------|--------------------|--------------------|--------------|----------------|---|-----|
| 1 | | Contracts | 1 day | Thu 4/12/12 | Thu 4/12/12 | | | | |
| 2 | | Supply Construction Agreement | 2 hrs | Thu 4/12/12 | Thu 4/12/12 | | Builder | | |
| 3 | | Supply Contract Plans | 2 hrs | Thu 4/12/12 | Thu 4/12/12 | 2 | Builder | | |
| 4 | | Supply Contract Specifications | 2 hrs | Thu 4/12/12 | Thu 4/12/12 | 3 | Builder | | |
| 5 | | Supply Contract Site Plan | 2 hrs | Thu 4/12/12 | Thu 4/12/12 | 4 | Builder | | |
| 6 | | | | | | | | | |
| 7 | | Documentation | 9 days | Fri 4/13/12 | Wed 4/25/12 | | | | |
| 8 | | Review & Finalize Plans | 2 days | Fri 4/13/12 | Mon 4/16/12 | 3 | Builder | | |
| 9 | | Review & Finalize Specifications | 3 days | Tue 4/17/12 | Thu 4/19/12 | 4 | Builder | | |
| 10 | | Review & Finalize Site Plan | 1 day | Fri 4/20/12 | Fri 4/20/12 | 5 | Builder | | |
| 11 | | Print Construction Drawings | 2 days | Mon 4/23/12 | Tue 4/24/12 | 8,9,10 | Builder | | |
| 12 | | Approve Revised Plans & Specifications | 1 day | Wed 4/25/12 | Wed 4/25/12 | 11 | Client | | |
| 13 | | Documentation Complete | 0 days | Wed 4/25/12 | Wed 4/25/12 | 12 | | | |
| 14 | | | | | | | | | |
| 15 | | Bids & Contracts | 22 days | Thu 4/26/12 | Fri 5/25/12 | | | | |
| 16 | | Make Copies of Plans & Specifications | 2 days | Thu 4/26/12 | Fri 4/27/12 | 13 | Builder | | |
| 17 | | Distribute Plans & Specifications | 1 day | Mon 4/30/12 | Mon 4/30/12 | 16 | Builder | | |
| 18 | | Receive Bids | 10 days | Tue 5/1/12 | Mon 5/14/12 | 17 | Builder | | |
| 19 | | Review Bids | 4 days | Tue 5/15/12 | Fri 5/18/12 | 18 | Builder | | |
| 20 | | Execute Subcontractor Agreements | 5 days | Mon 5/21/12 | Fri 5/25/12 | 19 | Builder | | |
| 21 | | Bids & Contracts Complete | 0 days | Fri 5/25/12 | Fri 5/25/12 | 20 | | | |
| 22 | | | | | | | | | |
| 23 | | Order Materials | 1 day | Tue 5/29/12 | Tue 5/29/12 | | | | |
| 24 | | Order lumber, insulation, roofing materials, doors & windows | 4 hrs | Tue 5/29/12 | Tue 5/29/12 | 21 | Builder | | |
| 25 | | Order trusses | 1 hr | Tue 5/29/12 | Tue 5/29/12 | 24 | Builder | | |

| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors | Resource Names | 3 | |
|----|-----------|---|----------------|--------------------|--------------------|--------------|----------------------------|-----|--|
| | | | | | | | | Thu | |
| 26 | | Order drywall | 1 hr | Tue 5/29/12 | Tue 5/29/12 | 25 | Builder | | |
| 27 | | Order pneumatic vacuum system & heating units | 2 hrs | Tue 5/29/12 | Tue 5/29/12 | 26 | Builder | | |
| 28 | | | | | | | | | |
| 29 | | Grading & Building Permits | 13 days | Wed 5/30/12 | Fri 6/15/12 | | | | |
| 30 | | Schedule lot stake-out | 1 hr | Wed 5/30/12 | Wed 5/30/12 | 21 | Builder | | |
| 31 | | Stake lot | 1 day | Mon 6/4/12 | Mon 6/4/12 | 30 | Civil Engineer | | |
| 32 | | File Grading Permit Application | 1 day | Thu 5/31/12 | Thu 5/31/12 | 21 | Builder | | |
| 33 | | File Building Permit Application | 2 days | Thu 5/31/12 | Fri 6/1/12 | 21 | Builder | | |
| 34 | | Post Lot Identification | 1 hr | Mon 6/4/12 | Mon 6/4/12 | 33 | Builder | | |
| 35 | | Meet Sediment Control Inspector | 1 day | Tue 6/5/12 | Tue 6/5/12 | 32 | Builder | | |
| 36 | | Install Sediment Controls | 2 days | Wed 6/6/12 | Thu 6/7/12 | 35 | Builder | | |
| 37 | | Sediment Control Inspection | 1 day | Fri 6/8/12 | Fri 6/8/12 | 36 | Sediment Control Inspector | | |
| 38 | | Grading Permit Issued | 1 day | Mon 6/11/12 | Mon 6/11/12 | 37 | Sediment Control Inspector | | |
| 39 | | County Permit Process | 10 days | Thu 5/31/12 | Wed 6/13/12 | 21 | Department of Permits | | |
| 40 | | Building Permit Approved | 1 day | Thu 6/14/12 | Thu 6/14/12 | 39 | Department of Permits | | |
| 41 | | Pay Permit Fees and Excise Taxes | 1 day | Fri 6/15/12 | Fri 6/15/12 | 40 | Builder | | |
| 42 | | Building Permit Issued | 0 days | Fri 6/15/12 | Fri 6/15/12 | 41 | | | |
| 43 | | | | | | | | | |
| 44 | | Site Work | 4 days | Fri 6/15/12 | Wed 6/20/12 | | | | |
| 45 | | Clear Lot | 1 day | Fri 6/15/12 | Fri 6/15/12 | 38,39 | Excavation Subcontractor | | |
| 46 | | Strip Topsoil & Stockpile | 1 day | Mon 6/18/12 | Mon 6/18/12 | 45 | Excavation Subcontractor | | |
| 47 | | Stake Lot for Excavation | 1 day | Mon 6/18/12 | Mon 6/18/12 | 45 | Civil Engineer | | |
| 48 | | Rough Grade Lot | 1 day | Tue 6/19/12 | Tue 6/19/12 | 47 | Excavation Subcontractor | | |
| 49 | | Excavate for Foundation | 1 day | Wed 6/20/12 | Wed 6/20/12 | 48 | Excavation Subcontractor | | |
| 50 | | | | | | | | | |

Project: bruce_workshop_030320
Date: Thu 8/2/12

| | | | | | |
|-----------------|--|--------------------|--|-----------------------|--|
| Task | | External Milestone | | Manual Summary Rollup | |
| Split | | Inactive Task | | Manual Summary | |
| Milestone | | Inactive Milestone | | Start-only | |
| Summary | | Inactive Summary | | Finish-only | |
| Project Summary | | Manual Task | | Deadline | |
| External Tasks | | Duration-only | | Progress | |

| ID | | Task Mode | Task Name | Duration | Start | Finish | Predecessors | Resource Names | | Thu |
|----|--|-----------|--------------------------------------|----------------|--------------------|--------------------|--------------|--------------------------|---|-----|
| | | | | | | | | | 3 | |
| 51 | | | Foundation | 5 days | Thu 6/21/12 | Thu 6/28/12 | | | | |
| 52 | | | Layout footings | 1 day | Thu 6/21/12 | Thu 6/21/12 | 49 | Concrete Subcontractor | | |
| 53 | | | Dig Footings and Install Reinforcing | 2 days | Fri 6/22/12 | Mon 6/25/12 | 52 | Concrete Subcontractor | | |
| 54 | | | Footing Inspection | 0 days | Tue 6/26/12 | Tue 6/26/12 | 53 | Building Inspector | | |
| 55 | | | Pour footings and foundation | 1 day | Tue 6/26/12 | Tue 6/26/12 | 54 | Concrete Subcontractor | | |
| 56 | | | Pin footings | 1 day | Wed 6/27/12 | Wed 6/27/12 | 55 | Civil Engineer | | |
| 57 | | | Foundation Complete | 0 days | Thu 6/28/12 | Thu 6/28/12 | 56 | | | |
| 58 | | | | | | | | | | |
| 59 | | | Raise Building | 9 days | Fri 6/29/12 | Thu 7/12/12 | | | | |
| 60 | | | Lumber delivery | 1 day | Fri 6/29/12 | Fri 6/29/12 | 57 | Lumber Supplier | | |
| 61 | | | Frame walls | 1 day | Mon 7/2/12 | Mon 7/2/12 | 60 | Builder | | |
| 62 | | | Truss delivery | 1 day | Fri 6/29/12 | Fri 6/29/12 | | Truss Supplier | | |
| 63 | | | Install roof trusses | 1 day | Tue 7/3/12 | Tue 7/3/12 | 61,62 | Builder | | |
| 64 | | | Framework Inspection | 0 days | Wed 7/4/12 | Wed 7/4/12 | 61,63 | Building Inspector | | |
| 65 | | | Insulation delivery | 1 day | Tue 7/3/12 | Tue 7/3/12 | 61 | Insulation Supplier | | |
| 66 | | | Install external insulation sheets | 1 day | Wed 7/4/12 | Wed 7/4/12 | 65 | Builder | | |
| 67 | | | Install exterior siding & roof | 2 days | Thu 7/5/12 | Fri 7/6/12 | 66 | Builder | | |
| 68 | | | Roofing materials delivery | 1 day | Wed 7/4/12 | Wed 7/4/12 | 63 | Roofing Supplier | | |
| 69 | | | Install Roof Vents | 1 day | Mon 7/9/12 | Mon 7/9/12 | 67 | Builder | | |
| 70 | | | Install tar paper/shingles | 2 days | Tue 7/10/12 | Wed 7/11/12 | 68,69 | Builder | | |
| 71 | | | Structure Inspection | 0 days | Thu 7/12/12 | Thu 7/12/12 | 67,70 | Building Inspector | | |
| 72 | | | | | | | | | | |
| 73 | | | Electrical | 21 days | Mon 6/18/12 | Tue 7/17/12 | | | | |
| 74 | | | Schedule PUD for utilities hookup | 1 day | Mon 6/18/12 | Mon 6/18/12 | 42 | Builder | | |
| 75 | | | Heating units delivery | 1 day | Tue 7/3/12 | Tue 7/3/12 | 61 | Heating Supplier | | |
| 76 | | | Install Breaker box | 4 hrs | Thu 7/5/12 | Thu 7/5/12 | 61 | Electrical Subcontractor | | |


| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors | Resource Names | 3 | |
|-----|-----------|---------------------------------------|---------------|--------------------|--------------------|--------------|--------------------------|---|-----|
| | | | | | | | | | Thu |
| 77 | | Install heating units & thermostat | 4 hrs | Thu 7/5/12 | Thu 7/5/12 | 75,79 | Electrical Subcontractor | | |
| 78 | | PUD utilities hookup | 1 day | Fri 7/6/12 | Fri 7/6/12 | 76 | PUD | | |
| 79 | | Install wiring, outlets, and fixtures | 1 day | Fri 7/6/12 | Fri 7/6/12 | 76 | Electrical Subcontractor | | |
| 80 | | Electrical Inspection | 1 hr | Fri 7/6/12 | Fri 7/6/12 | 76,77,78,79 | Building Inspector | | |
| 81 | | Electrical Complete | 0 days | Fri 7/6/12 | Fri 7/6/12 | 80 | | | |
| 82 | | | | | | | | | |
| 83 | | Doors/Windows | 6 days | Mon 7/9/12 | Tue 7/17/12 | | | | |
| 84 | | Window/Door delivery | 1 day | Mon 7/9/12 | Mon 7/9/12 | 67 | Window/Door Supplier | | |
| 85 | | Install Windows | 4 hrs | Thu 7/12/12 | Thu 7/12/12 | 84 | Builder | | |
| 86 | | Install Exterior Entry Door | 4 hrs | Thu 7/12/12 | Thu 7/12/12 | 84 | Builder | | |
| 87 | | Install Garage Door | 1 day | Fri 7/13/12 | Fri 7/13/12 | 84 | Builder | | |
| 88 | | Install external trim | 1 day | Mon 7/16/12 | Mon 7/16/12 | 85,86,87 | Builder | | |
| 89 | | Installation Inspection | 0 days | Tue 7/17/12 | Tue 7/17/12 | 88 | Building Inspector | | |
| 90 | | | | | | | | | |
| 91 | | Drywall Installation | 9 days | Thu 7/12/12 | Tue 7/24/12 | | | | |
| 92 | | Drywall delivery | 1 day | Thu 7/12/12 | Thu 7/12/12 | 70 | Drywall Supplier | | |
| 93 | | Install insulation | 1 day | Tue 7/17/12 | Tue 7/17/12 | 65 | Builder | | |
| 94 | | Install drywall | 2 days | Wed 7/18/12 | Thu 7/19/12 | 92,93 | Drywall Subcontractor | | |
| 95 | | Drywall Inspection | 0 days | Fri 7/20/12 | Fri 7/20/12 | 94 | Building Inspector | | |
| 96 | | Mud drywall | 1 day | Fri 7/20/12 | Fri 7/20/12 | 95 | Drywall Subcontractor | | |
| 97 | | Sand and finish drywall | 2 days | Mon 7/23/12 | Tue 7/24/12 | 96 | Drywall Subcontractor | | |
| 98 | | | | | | | | | |
| 99 | | Finish | 6 days | Wed 7/25/12 | Wed 8/1/12 | | | | |
| 100 | | Cabinetry delivery | 1 day | Wed 7/25/12 | Wed 7/25/12 | 97 | Cabinet Supplier | | |
| 101 | | Install internal trim | 1 day | Wed 7/25/12 | Wed 7/25/12 | 97 | Builder | | |
| 102 | | Paint Interior | 1 day | Thu 7/26/12 | Thu 7/26/12 | 101 | Builder | | |


Project: bruce_workshop_030320
Date: Thu 8/2/12

| | | | | | |
|-----------------|--|--------------------|--|-----------------------|--|
| Task | | External Milestone | | Manual Summary Rollup | |
| Split | | Inactive Task | | Manual Summary | |
| Milestone | | Inactive Milestone | | Start-only | |
| Summary | | Inactive Summary | | Finish-only | |
| Project Summary | | Manual Task | | Deadline | |
| External Tasks | | Duration-only | | Progress | |


| ID | Task Mode | Task Name | Duration | Start | Finish | Predecessors | Resource Names | | |
|-----|-----------|----------------------------------|---------------|-------------------|-------------------|--------------|------------------------|---|-----|
| | | | | | | | | 3 | Thu |
| 103 | | Paint Exterior | 1 day | Fri 7/27/12 | Fri 7/27/12 | 88 | Builder | | |
| 104 | | Vacuum system delivery | 1 day | Fri 7/27/12 | Fri 7/27/12 | 97 | Vacuum System Supplier | | |
| 105 | | Install Vacuum System | 1 day | Mon 7/30/12 | Mon 7/30/12 | 104 | Builder | | |
| 106 | | Install Vacuum ducts | 1 day | Tue 7/31/12 | Tue 7/31/12 | 105 | Builder | | |
| 107 | | Install cabinets and workbenches | 1 day | Wed 8/1/12 | Wed 8/1/12 | 106 | Builder | | |
| 108 | | | | | | | | | |
| 109 | | Completion | 2 days | Thu 8/2/12 | Fri 8/3/12 | | | | |
| 110 | | Final Site Cleanup | 1 day | Thu 8/2/12 | Thu 8/2/12 | 107 | Builder | | |
| 111 | | Customer Walkthru/Buyoff | 1 day | Fri 8/3/12 | Fri 8/3/12 | 110 | Client | | |
| 112 | | Project Complete | 0 days | Fri 8/3/12 | Fri 8/3/12 | 111 | | | |



| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

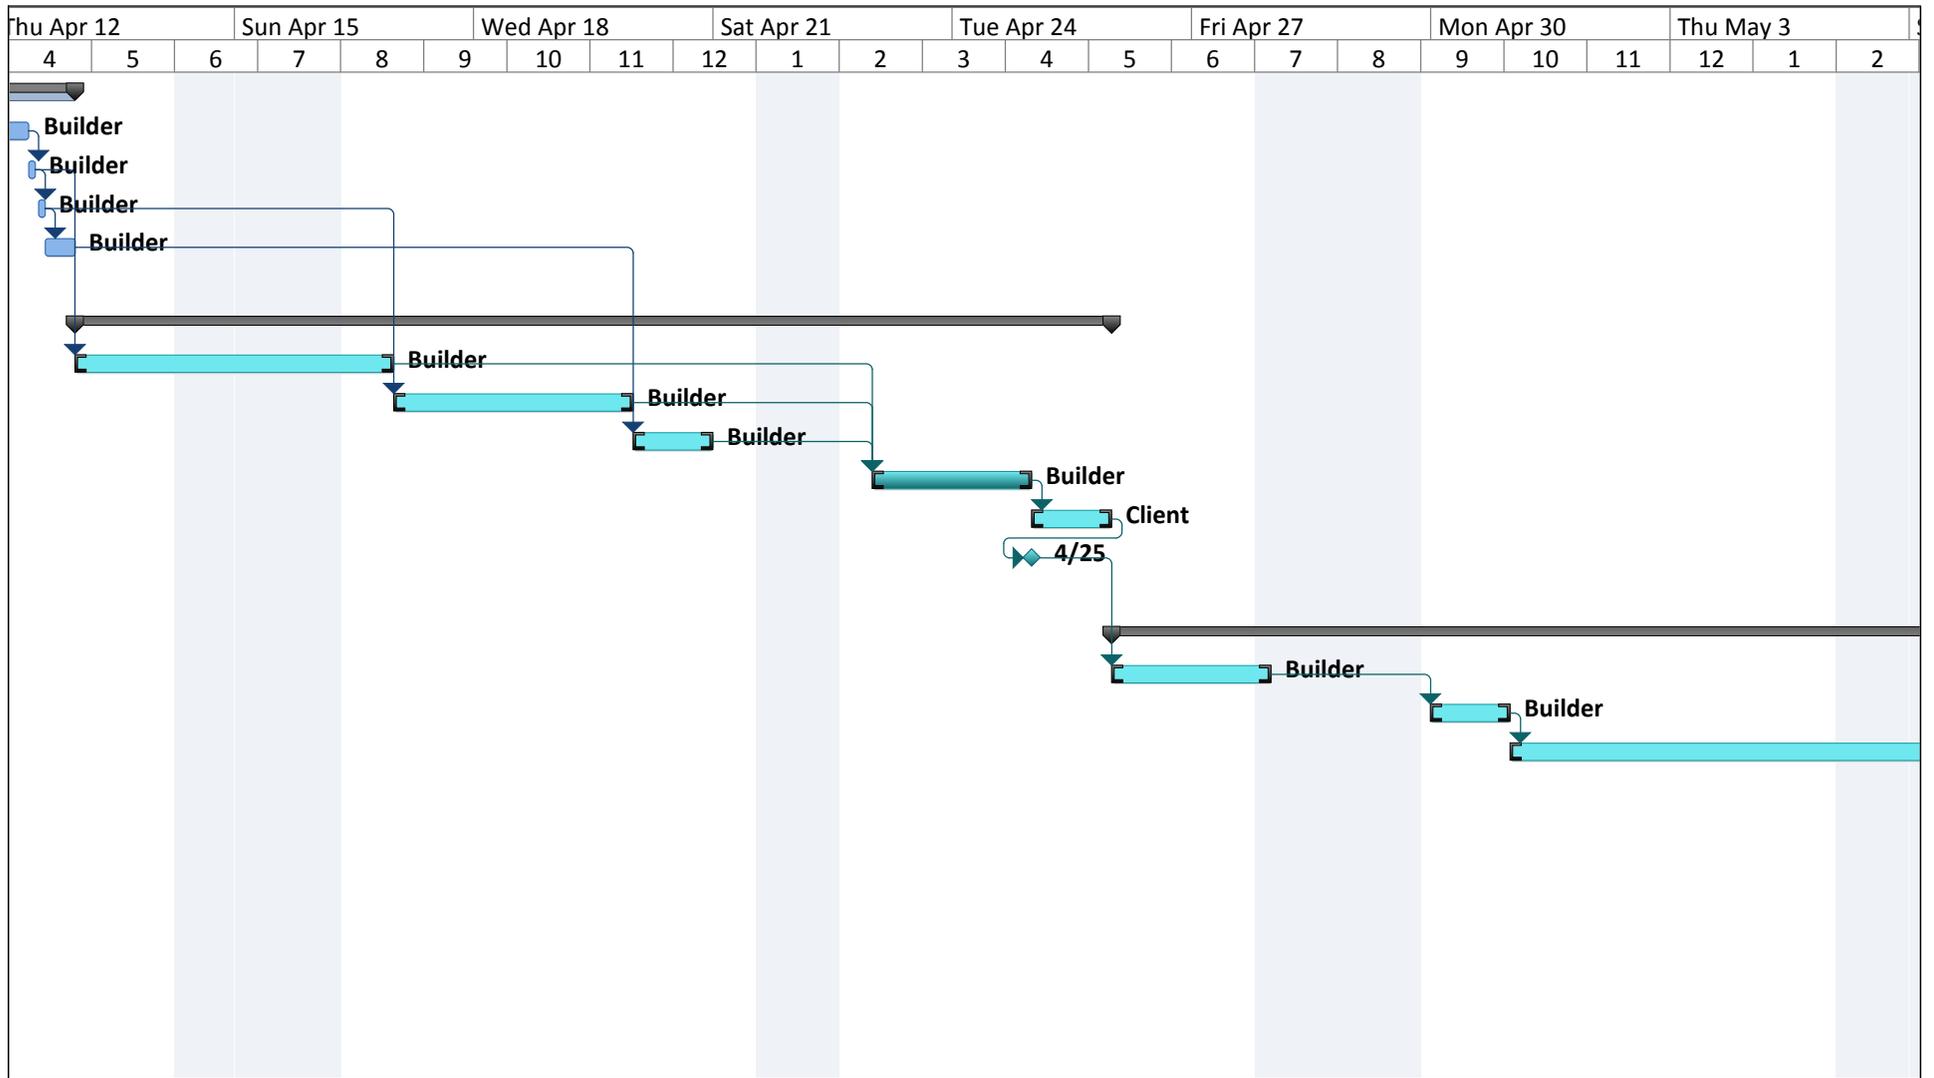


| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |




Project: bruce_workshop_030320
Date: Thu 8/2/12

| | | | | | |
|-----------------|--|--------------------|--|-----------------------|--|
| Task | | External Milestone | | Manual Summary Rollup | |
| Split | | Inactive Task | | Manual Summary | |
| Milestone | | Inactive Milestone | | Start-only | |
| Summary | | Inactive Summary | | Finish-only | |
| Project Summary | | Manual Task | | Deadline | |
| External Tasks | | Duration-only | | Progress | |




| | | | | | | |
|--|-----------------|---|--------------------|---|-----------------------|---|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task |  | External Milestone |  | Manual Summary Rollup |  |
| | Split |  | Inactive Task |  | Manual Summary |  |
| | Milestone |  | Inactive Milestone |  | Start-only |  |
| | Summary |  | Inactive Summary |  | Finish-only |  |
| | Project Summary |  | Manual Task |  | Deadline |  |
| | External Tasks |  | Duration-only |  | Progress |  |



| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |


| Thu Apr 12 | | Sun Apr 15 | | | Wed Apr 18 | | | Sat Apr 21 | | | Tue Apr 24 | | | Fri Apr 27 | | | Mon Apr 30 | | | Thu May 3 | | |
|------------|---|------------|---|---|------------|----|----|------------|---|---|------------|---|---|------------|---|---|------------|----|----|-----------|---|---|
| 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 1 | 2 |
| | | | | | | | | | | | | | | | | | | | | | | |

| | | | | | | |
|--|-----------------|---|--------------------|---|-----------------------|---|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task |  | External Milestone |  | Manual Summary Rollup |  |
| | Split |  | Inactive Task |  | Manual Summary |  |
| | Milestone |  | Inactive Milestone |  | Start-only |  |
| | Summary |  | Inactive Summary |  | Finish-only |  |
| | Project Summary |  | Manual Task |  | Deadline |  |
| | External Tasks |  | Duration-only |  | Progress |  |

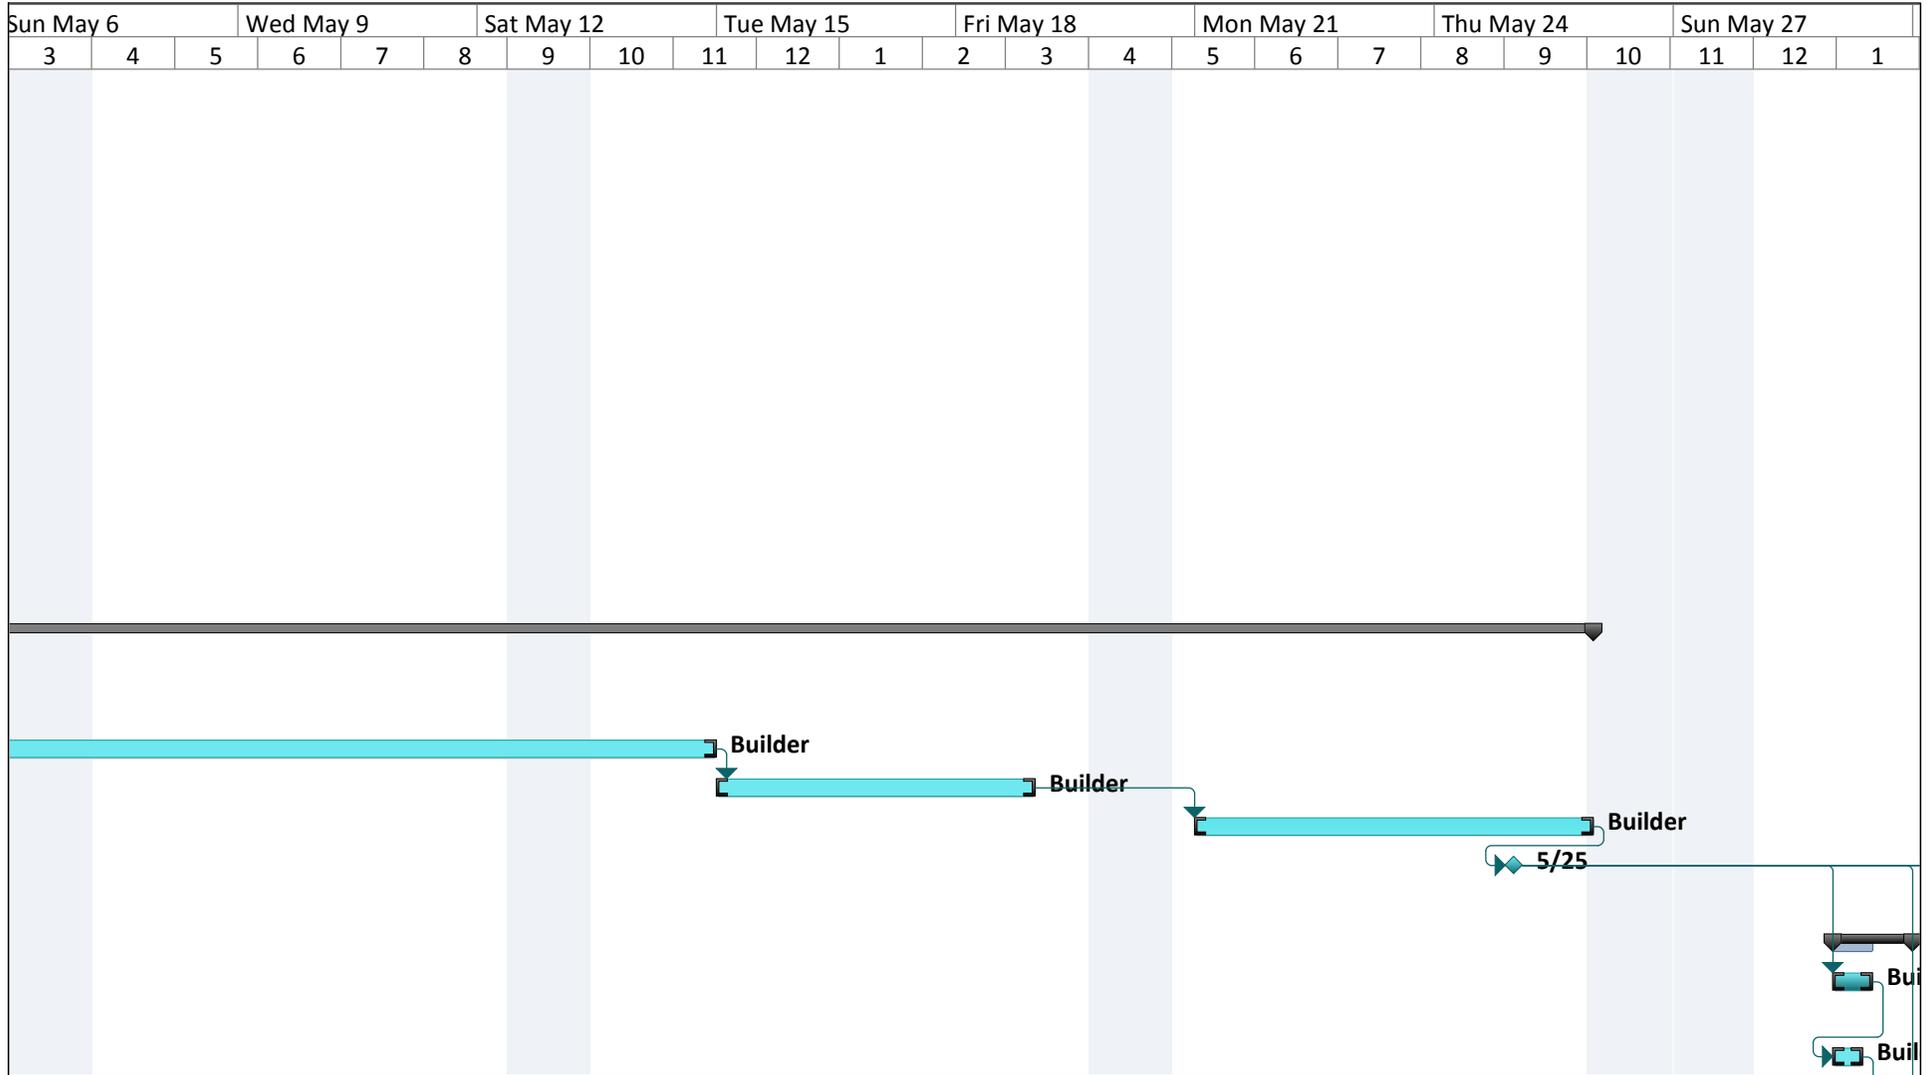


Project: bruce_workshop_030320
 Date: Thu 8/2/12

| | | | | | |
|-----------------|--|--------------------|--|-----------------------|--|
| Task | | External Milestone | | Manual Summary Rollup | |
| Split | | Inactive Task | | Manual Summary | |
| Milestone | | Inactive Milestone | | Start-only | |
| Summary | | Inactive Summary | | Finish-only | |
| Project Summary | | Manual Task | | Deadline | |
| External Tasks | | Duration-only | | Progress | |

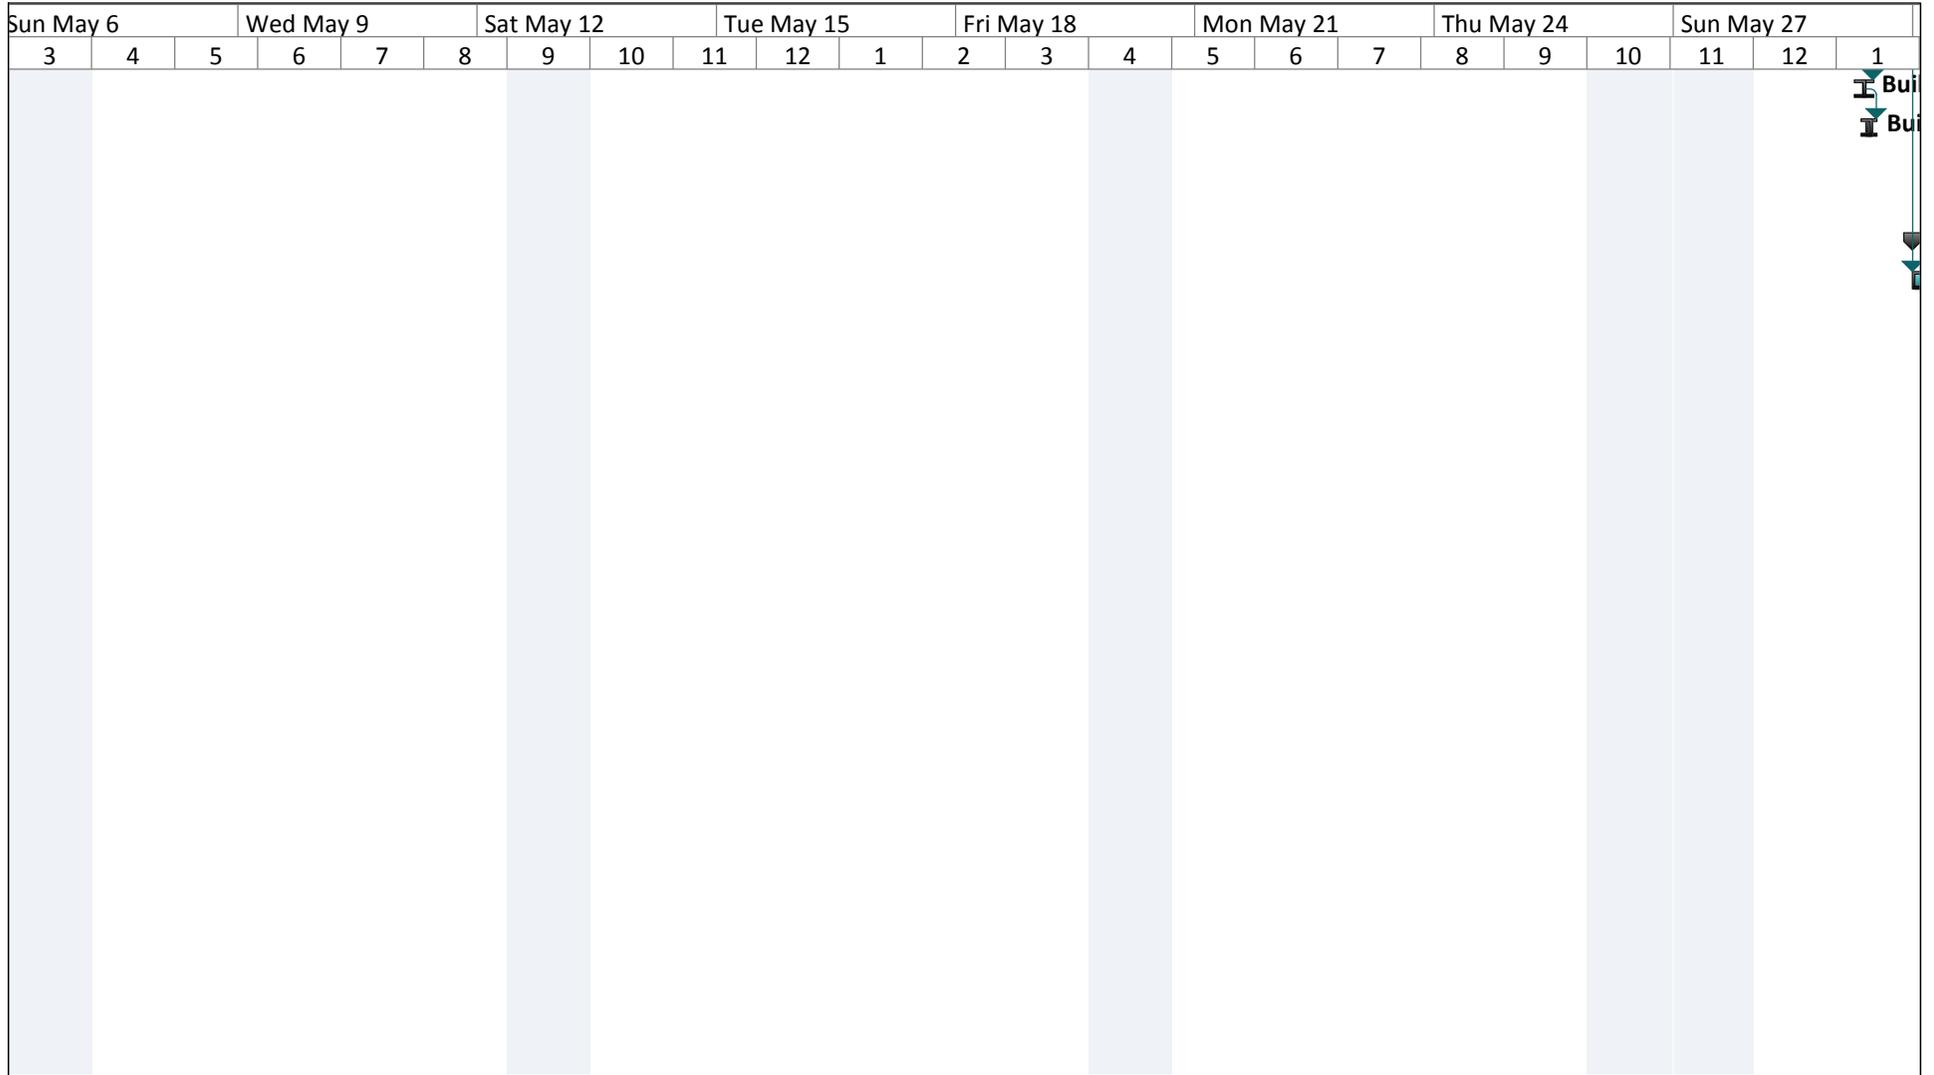


Project: bruce_workshop_030320
 Date: Thu 8/2/12

| | | | | | |
|-----------------|--|--------------------|--|-----------------------|--|
| Task | | External Milestone | | Manual Summary Rollup | |
| Split | | Inactive Task | | Manual Summary | |
| Milestone | | Inactive Milestone | | Start-only | |
| Summary | | Inactive Summary | | Finish-only | |
| Project Summary | | Manual Task | | Deadline | |
| External Tasks | | Duration-only | | Progress | |




| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |




| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

| Sun May 6 | | | Wed May 9 | | | Sat May 12 | | | Tue May 15 | | | Fri May 18 | | | Mon May 21 | | | Thu May 24 | | | Sun May 27 | | |
|-----------|---|---|-----------|---|---|------------|----|----|------------|---|---|------------|---|---|------------|---|---|------------|----|----|------------|---|--|
| 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 1 | |
| | | | | | | | | | | | | | | | | | | | | | | | |




| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |




uilder
uilder


| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

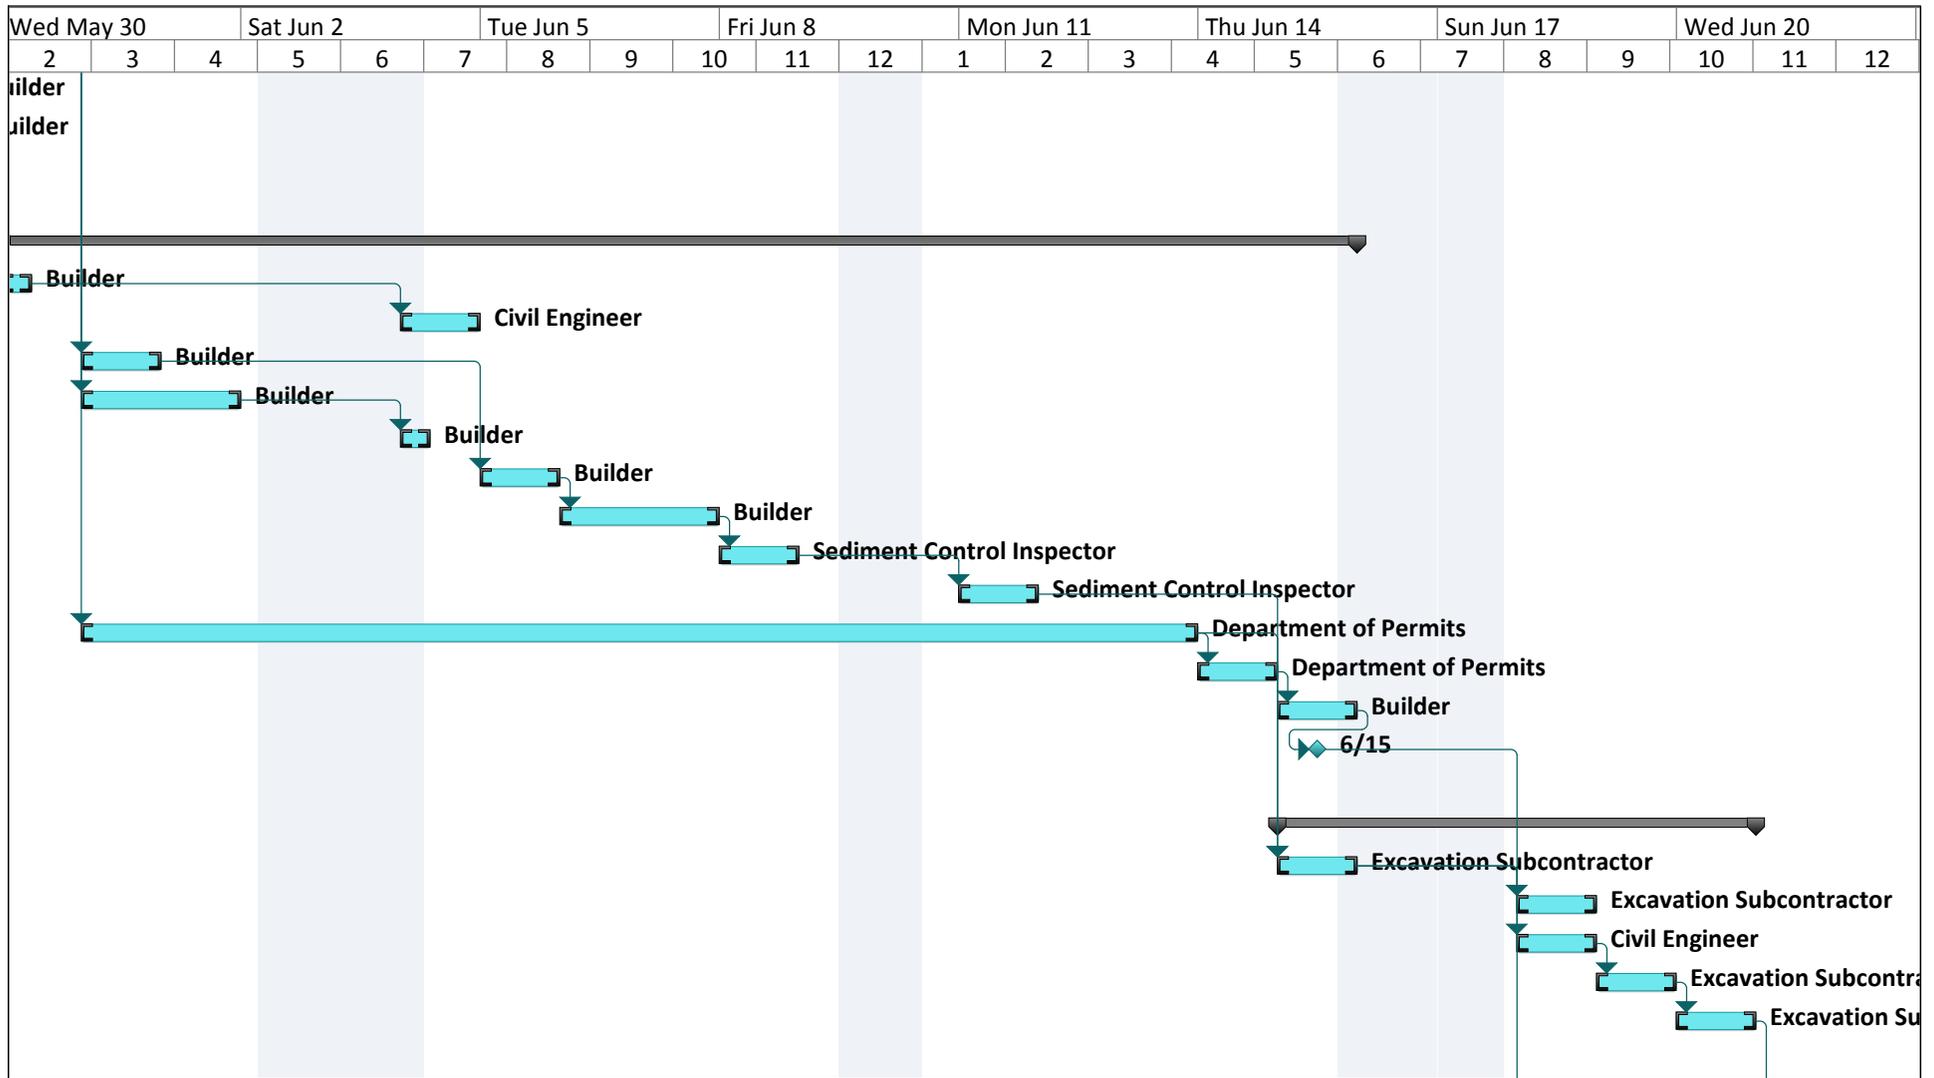

| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

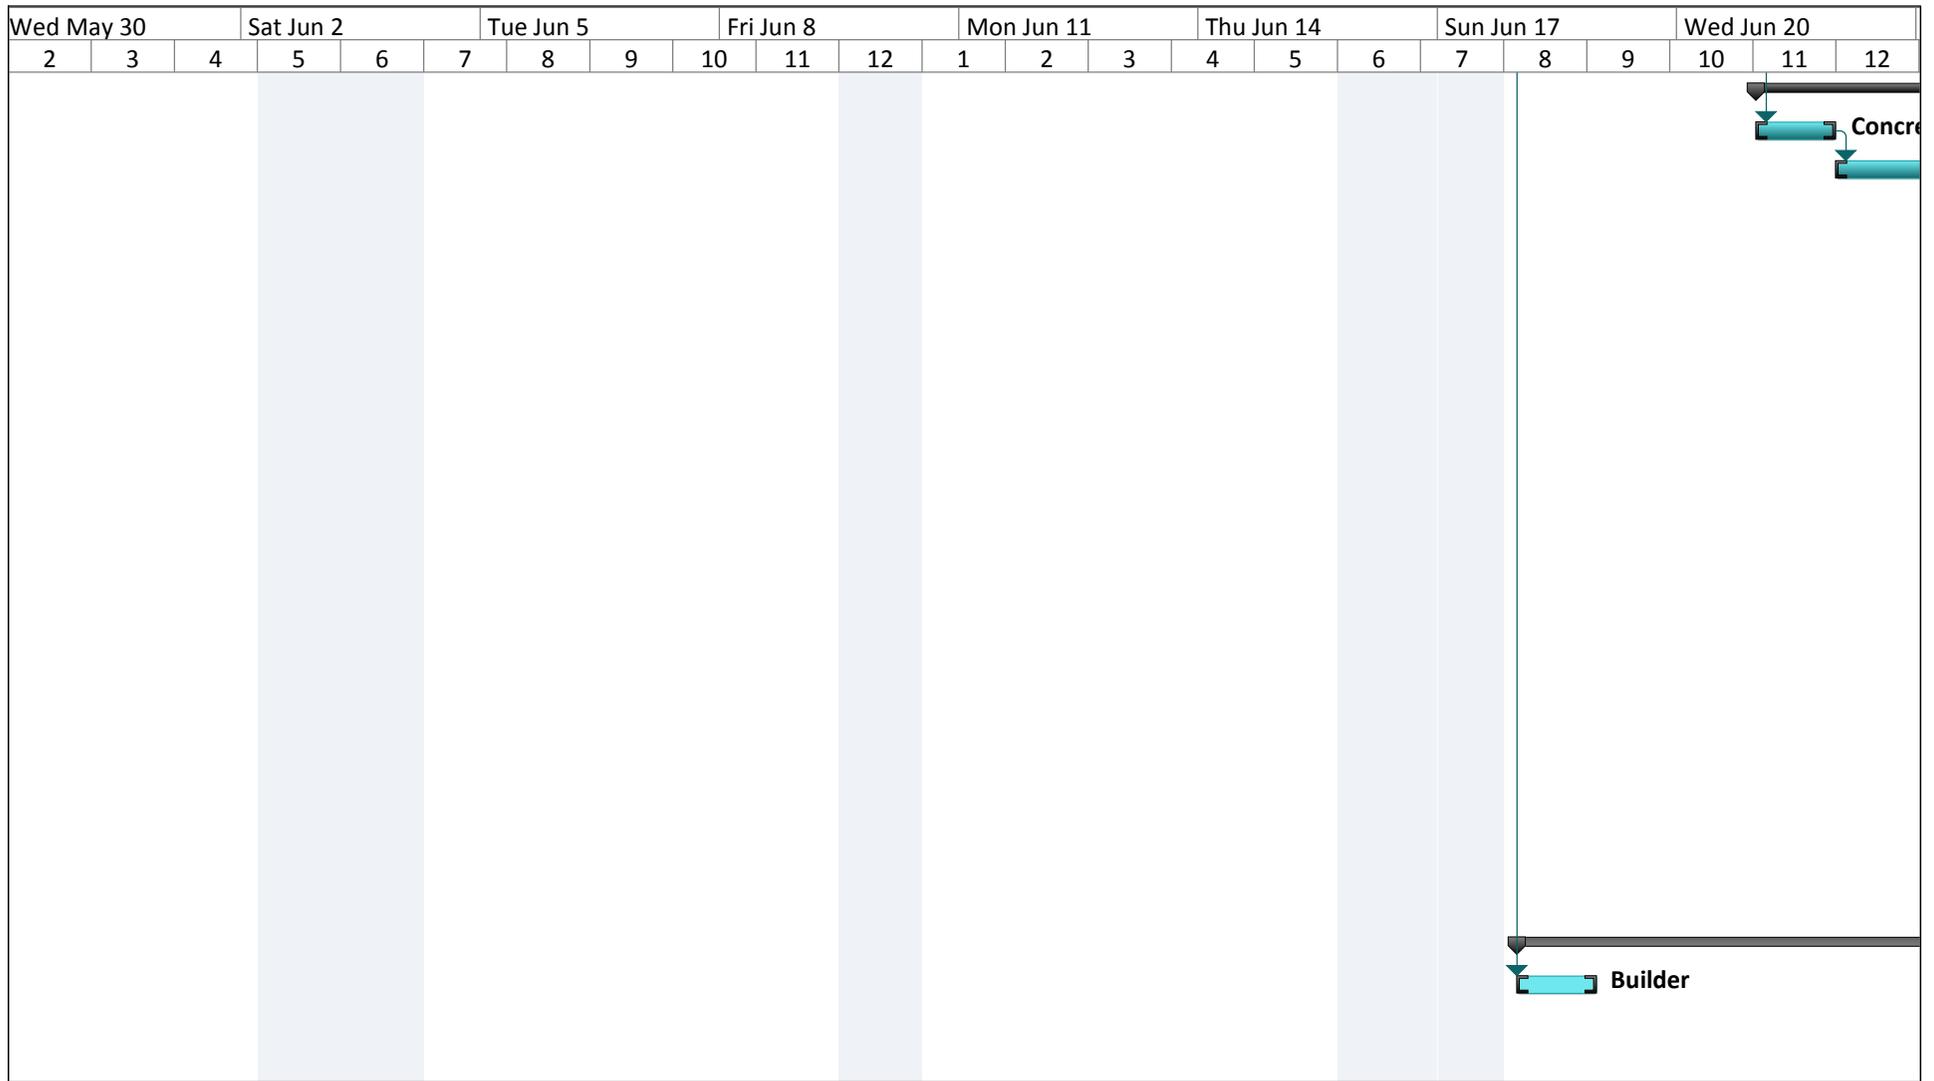

| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |



| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

| Wed May 30 | | | Sat Jun 2 | | | Tue Jun 5 | | | Fri Jun 8 | | | Mon Jun 11 | | | Thu Jun 14 | | | Sun Jun 17 | | | Wed Jun 20 | | |
|------------|---|---|-----------|---|---|-----------|---|----|-----------|----|--|------------|---|---|------------|---|---|------------|---|---|------------|----|----|
| 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 |
| | | | | | | | | | | | | | | | | | | | | | | | |


| | | | | | | |
|--|-----------------|---|--------------------|---|-----------------------|---|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task |  | External Milestone |  | Manual Summary Rollup |  |
| | Split |  | Inactive Task |  | Manual Summary |  |
| | Milestone |  | Inactive Milestone |  | Start-only |  |
| | Summary |  | Inactive Summary |  | Finish-only |  |
| | Project Summary |  | Manual Task |  | Deadline |  |
| | External Tasks |  | Duration-only |  | Progress |  |

| Sat Jun 23 | | | Tue Jun 26 | | | Fri Jun 29 | | | Mon Jul 2 | | | Thu Jul 5 | | | Sun Jul 8 | | | Wed Jul 11 | | | Sat Jul 14 | | |
|------------|---|---|------------|---|---|------------|---|---|-----------|----|----|-----------|---|---|-----------|---|---|------------|---|---|------------|----|--|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | |
| | | | | | | | | | | | | | | | | | | | | | | | |


| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

| Sat Jun 23 | | | Tue Jun 26 | | | Fri Jun 29 | | | Mon Jul 2 | | | Thu Jul 5 | | | Sun Jul 8 | | | Wed Jul 11 | | | Sat Jul 14 | | |
|--|---|---|------------|---|---|------------|---|---|-----------|----|----|-----------|---|---|-----------|---|---|------------|---|---|------------|----|--|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | |
| <div style="display: flex; justify-content: space-between; padding: 5px;"> Factor Subcontractor </div> | | | | | | | | | | | | | | | | | | | | | | | |

| | | | | | | |
|--|-----------------|---|--------------------|---|-----------------------|---|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task |  | External Milestone |  | Manual Summary Rollup |  |
| | Split |  | Inactive Task |  | Manual Summary |  |
| | Milestone |  | Inactive Milestone |  | Start-only |  |
| | Summary |  | Inactive Summary |  | Finish-only |  |
| | Project Summary |  | Manual Task |  | Deadline |  |
| | External Tasks |  | Duration-only |  | Progress |  |

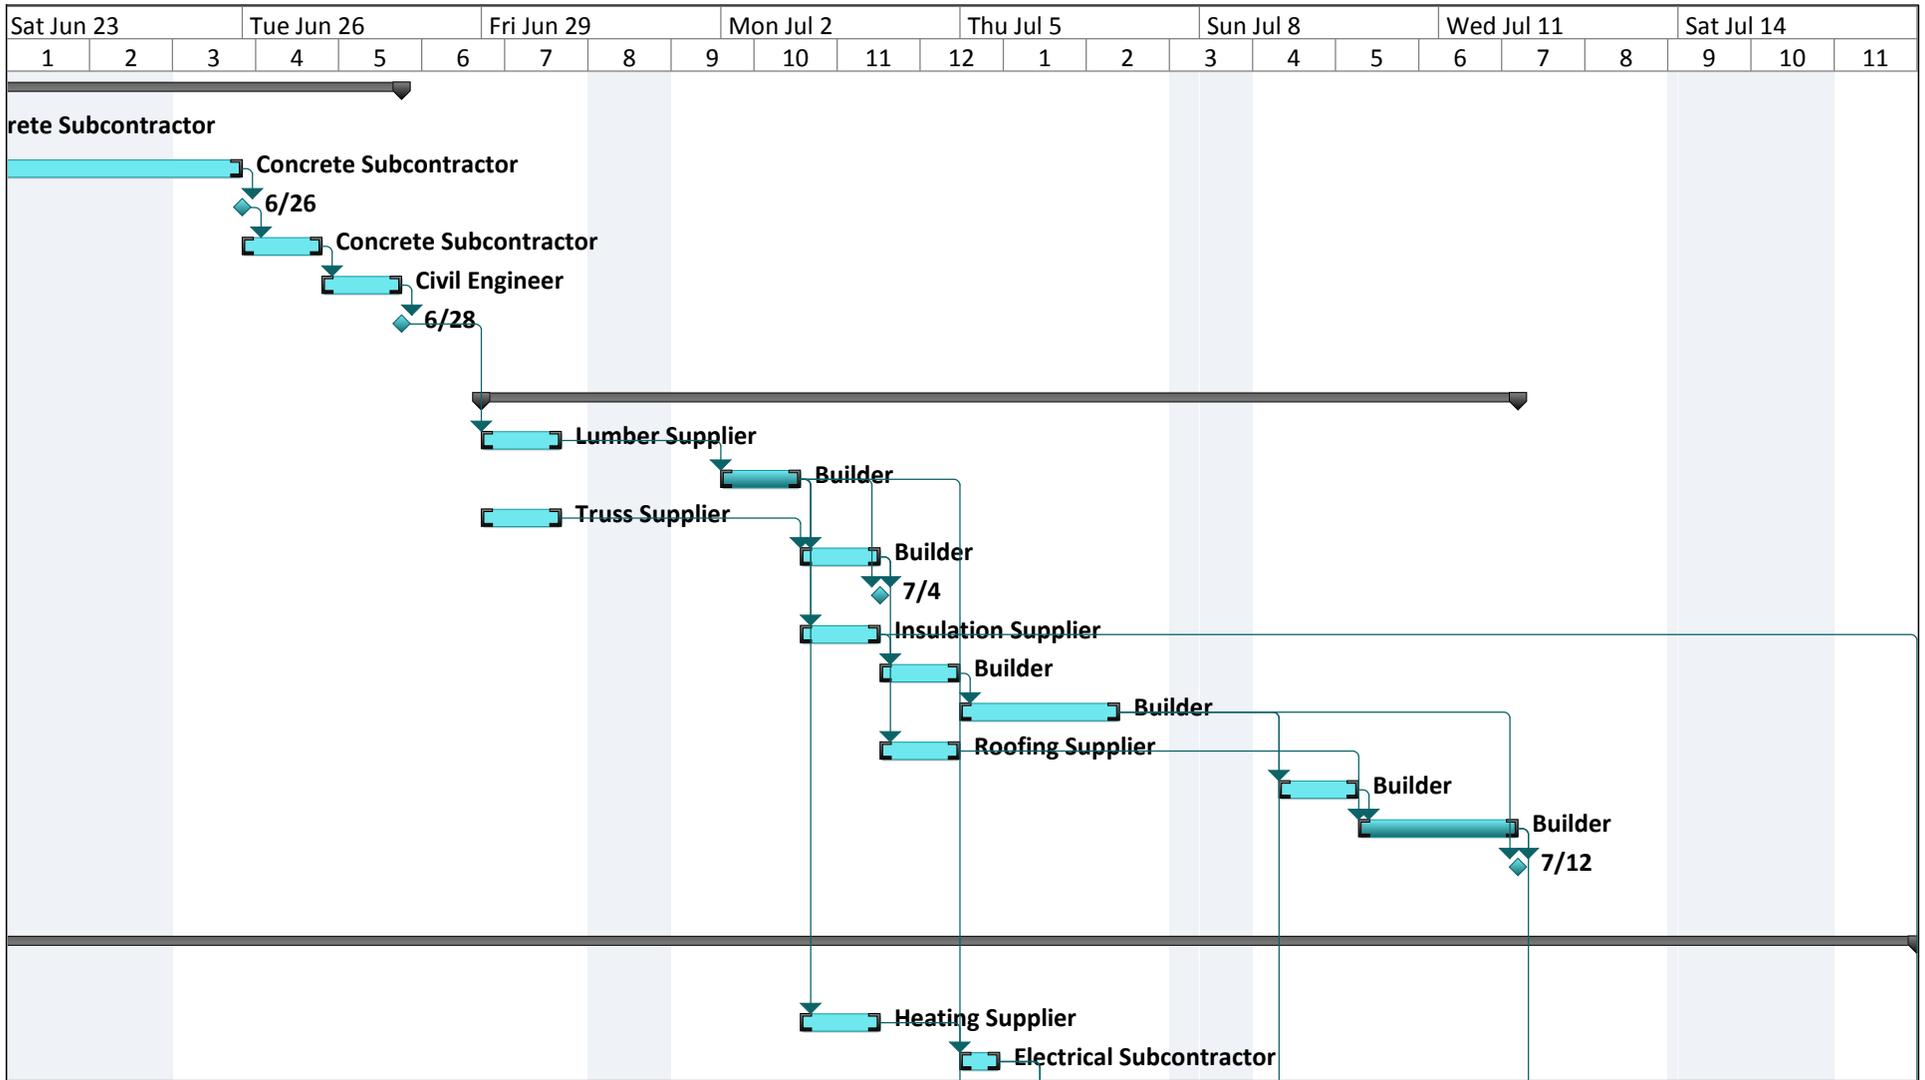


| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

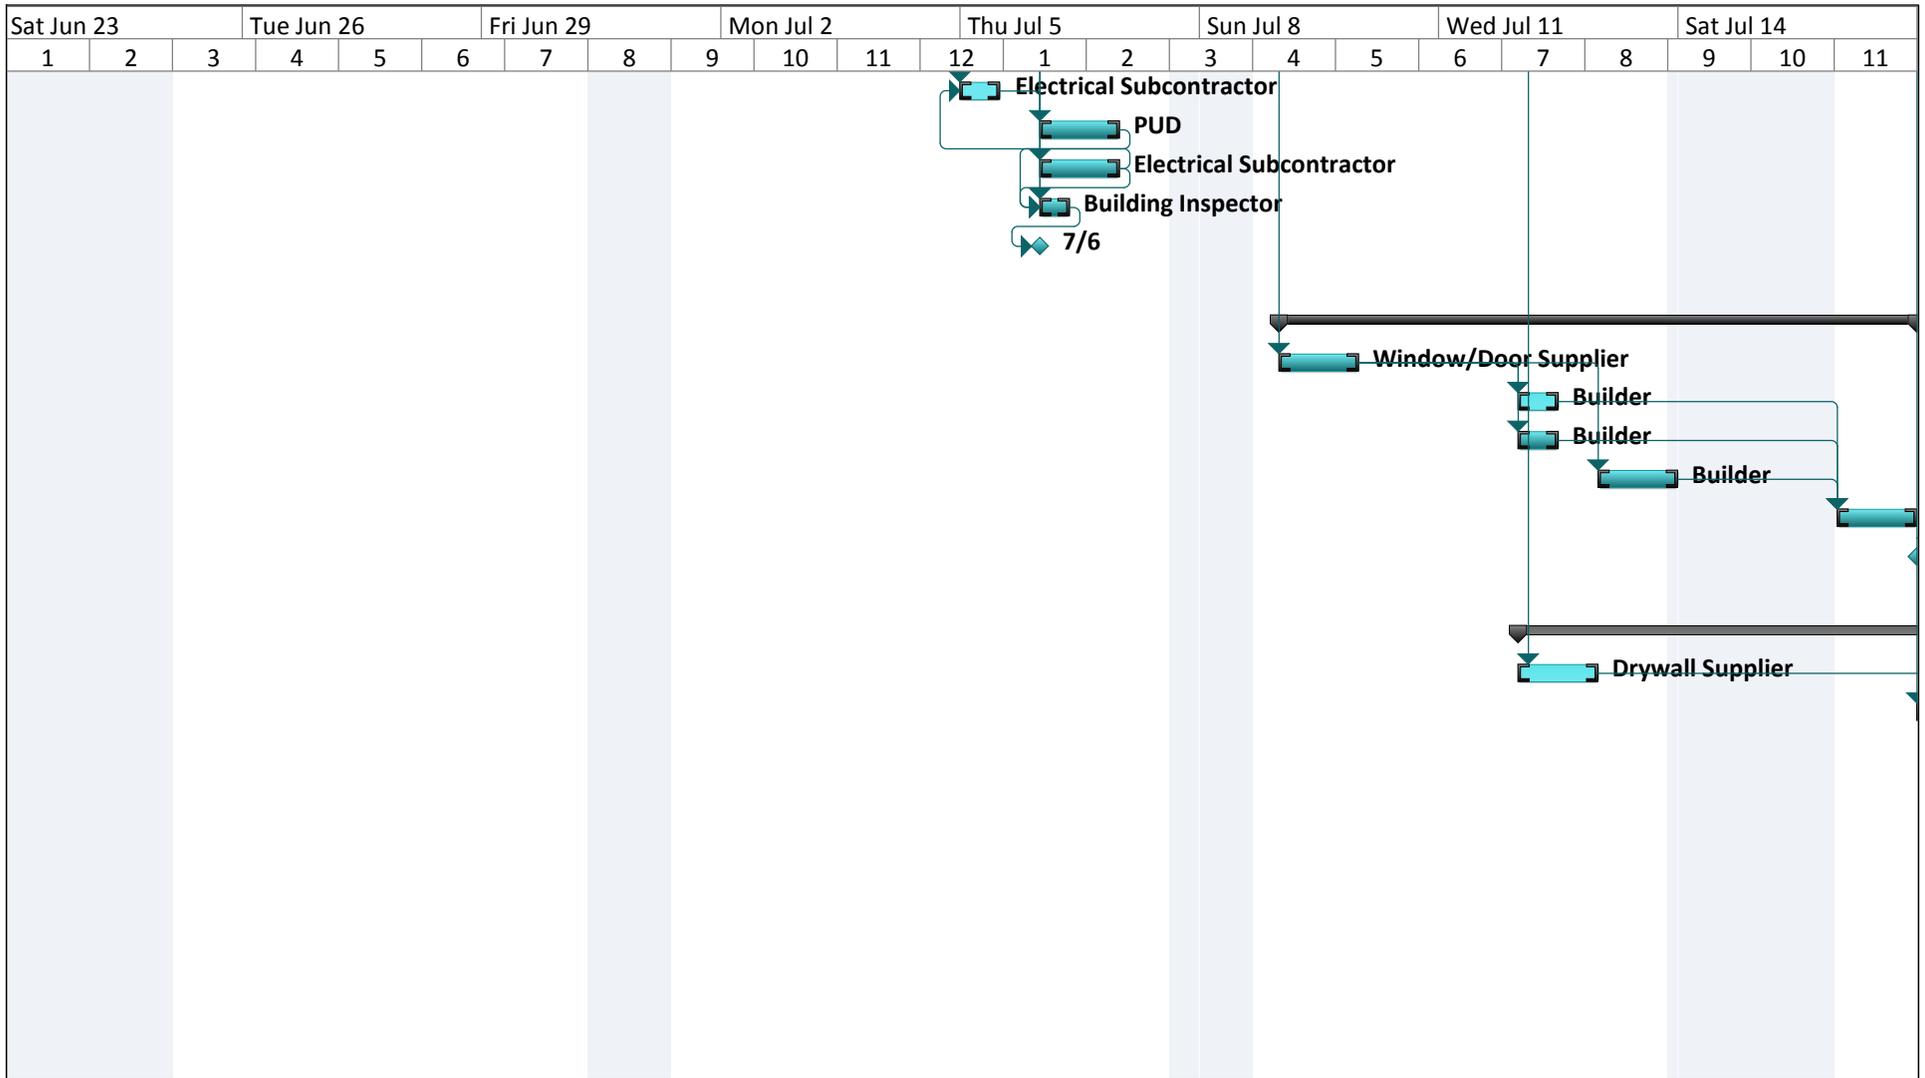


| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |


| Sat Jun 23 | | | Tue Jun 26 | | | Fri Jun 29 | | | Mon Jul 2 | | | Thu Jul 5 | | | Sun Jul 8 | | | Wed Jul 11 | | | Sat Jul 14 | | |
|------------|---|---|------------|---|---|------------|---|---|-----------|----|----|-----------|---|---|-----------|---|---|------------|---|---|------------|----|--|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | |
| | | | | | | | | | | | | | | | | | | | | | | | |




| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |




| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |




| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |



| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

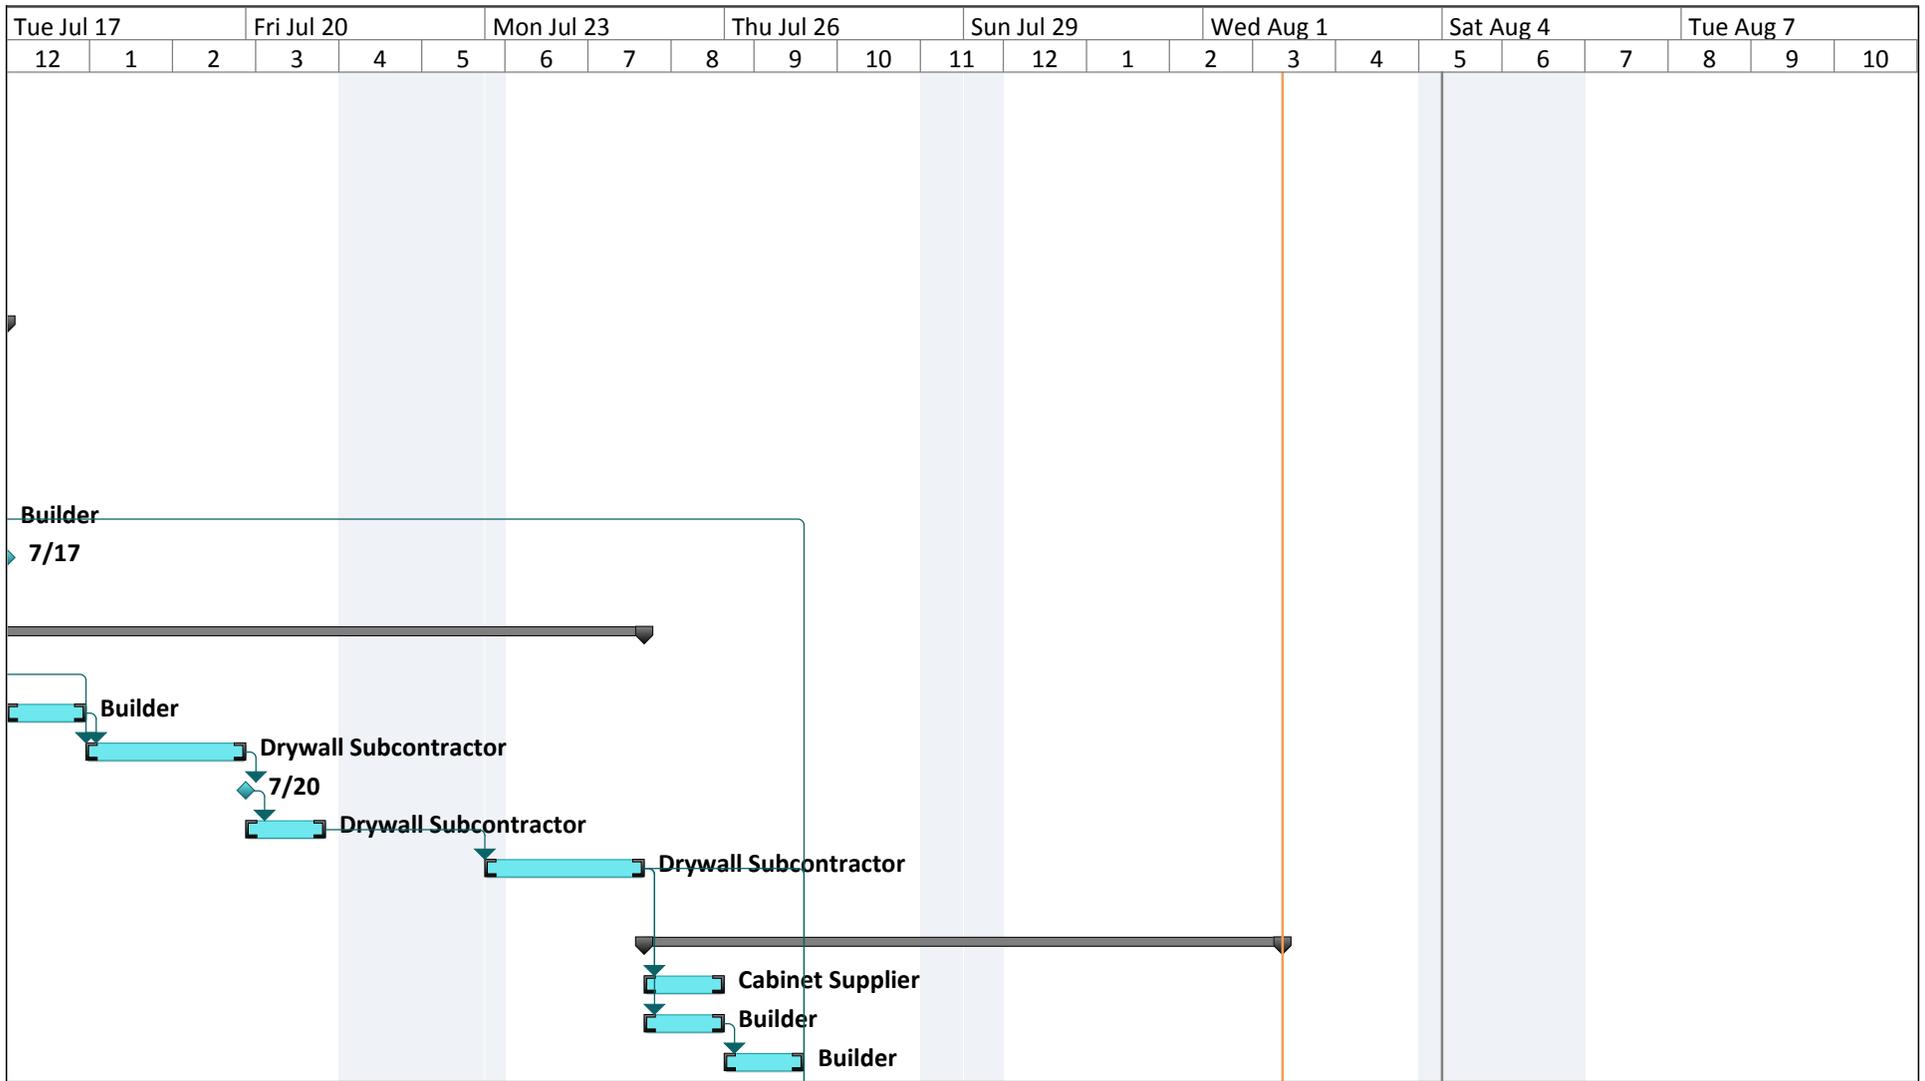

| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

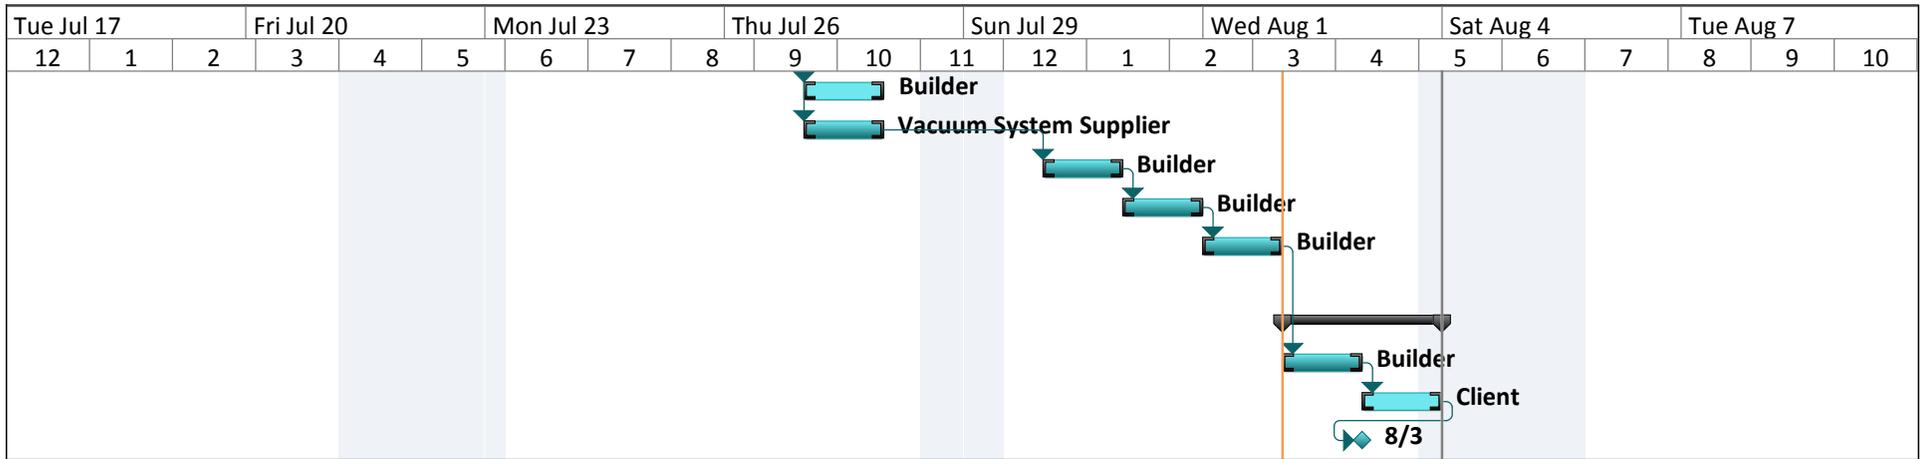

| | | | | | | |
|--|-----------------|--|--------------------|--|-----------------------|--|
| Project: bruce_workshop_030320 Date: Thu 8/2/12 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |
